Northern Line Extension Main Works Contract



CLIENT: LONDON UNDERGROUND LIMITED

CONTRACT REF: TLL 7917

NORTHERN LINE EXTENSION

MAIN WORKS CONTRACT

Battersea Unattended Noise Monitoring



Prepared by	Checked by	Approved by	Date	Rev
Jose Chicharro	Chris McCollin	Antony Gregson	22/12/17	34.0
Chighan	MIL	Andriffyer		

Northern Line Extension Main Works Contract

CONTENTS

1	Introduction	3
2	Monitoring Programme	4
2.1	Receptors	4
2.2	Monitoring Locations	4
2.3	Equipment	4
3	Noise Monitoring Results	5
4	Trigger Response Log	8
Арр	endix I – Site plan	9
	endix II – Northern Line Extension: Construction Noise and Vib	
Арр	endix III – Baseline survey	11
App	endix IV - Glossarv	13

DOC NO. FLO-N205-2360000-HSE-RPT-00010 Rev 34.0

Battersea Unattended Noise Monitoring Period 8 FY1718

Northern Line Extension Main Works Contract

1 INTRODUCTION

Ferrovial Laing O'Rourke (FLO) is currently undertaking works as part of the London Underground Extension of the Northern Line (NLE) running from Kennington to Battersea (Charing Cross branch).

Unattended noise monitoring stations have been set up in order to assess construction noise levels of the current activities at the nearest sensitive receptors located around the site boundary.

This report provides a summary of the unattended noise monitoring. The analysed monitoring period spanned hours between Sunday 15th October 2017 and Saturday 11th November 2017.

Northern Line Extension Main Works Contract

2 MONITORING PROGRAMME

2.1 Receptors

The unattended monitoring positions are representative of the following sensitive receptors:

- Residential receptors on Battersea Park Road (Viridian Apartments) (R1)
- Residential receptors on Battersea Park Road (Savona House) (R2)
- Residential receptors on Battersea Park Road (Duchess) (R3)
- Battersea Dogs & Cats Home (R4)

2.2 Monitoring Locations

Three monitoring units were installed on Friday 6th November 2015. The measurement positions are located within the NLE construction site at a height of approx. 2.9m and are considered to be free field measurements. They are illustrated in the layout plan presented in **Appendix I** and are as follows:

Table 1

MONITORING LOCATIONS									
Location	Coordinates	Representative sensitive receptor							
NLE site - South East (MP1)	529210, 177354	R1							
NLE site – South (MP2)	529111, 177269	R2, R3							
NLE site -West (MP3)	528945, 177260	R4							

2.3 Equipment

The measurement equipment used is detailed in **Table 2**. The measurement system was field calibrated before the start of the unattended monitoring and on-site calibrations are conducted monthly. All the measurement equipment is subject to current certificates of periodic validation traceable to national and international standards. Copies of calibration certificates are available upon request.

Table 2

SURVEY EQUIPMENT								
Manufacture	Item	Туре	Serial Number					
Sigicom	Sound Level Meter	INFRA S50	5565					
Sigicom	Sound Level Meter	INFRA S50	7376					
Sigicom	Sound Level Meter	INFRA S50	5343					

Northern Line Extension Main Works Contract

3 NOISE MONITORING RESULTS

The results of the monthly noise monitoring are presented below in **Table 3**, **Table 4** and **Table 5**. The measured noise levels have been corrected in order to predict noise levels from site activities at associated sensitive receptors. In addition, a façade correction which takes into account the reflections from the building façade of 3 dB(A) has been applied to the corrected noise levels.

The descriptions of the assessment periods are outlined in Appendix IV.

Table 3

Monthly N	loise Levels at R	1					
		Lmorn	Lday	Leve	Max LEN	Max LLN	Typical LLN
Sun	15/10/17	-	60.4	-	60.9	60.3	59.5
Mon	16/10/17	60.8	61.8	57.8	57.4	58.1	56.4
Tue	17/10/17	60.2	64.0	62.3	62.4	62.8	61.1
Wed	18/10/17	62.5	63.2	60.5	63.5	61.6	61.2
Thu	19/10/17	62.5	63.3	61.4	61.9	62.2	61.1
Fri	20/10/17	61.9	64.0	60.5	61.7	61.1	59.2
Sat	21/10/17	59.4	63.1	58.3	61.5	59.3	57.3
Sun	22/10/17	-	58.8	-	60.9	61.7	61.1
Mon	23/10/17	60.9	63.7	61.4	61.4	61.3	60.5
Tue	24/10/17	62.1	63.1	61.9	61.7	63.1	62.1
Wed	25/10/17	62.7	64.2	62.2	63.5	63.6	62.5
Thu	26/10/17	61.7	63.4	61.9	62.0	63.3	62.4
Fri	27/10/17	62.3	63.5	62.7	63.5	63.2	62.2
Sat	28/10/17	62.7	63.7	61.8	62.9	62.3	61.5
Sun	29/10/17	-	61.5	-	62.8	62.5	61.5
Mon	30/10/17	62.6	64.1	62.7	61.2	64.3	61.3
Tue	31/10/17	62.1	64.3	62.8	59.8	62.8	61.1
Wed	01/11/17	62.0	64.2	62.8	62.5	62.6	61.7
Thu	02/11/17	62.7	63.4	62.5	62.6	62.3	61.9
Fri	03/11/17	61.8	63.8	60.7	60.0	60.8	59.1
Sat	04/11/17	60.7	61.5	57.6	61.2	58.8	57.6
Sun	05/11/17	-	59.9	-	64.5	59.4	57.4
Mon	06/11/17	59.5	61.9	60.5	58.0	59.3	57.1
Tue	07/11/17	59.4	62.9	58.3	60.1	62.4	59.2
Wed	08/11/17	61.5	62.7	58.5	57.9	60.5	59.1
Thu	09/11/17	59.3	62.5	59.4	59.2	59.7	57.9
Fri	10/11/17	59.5	62.7	59.3	59.4	59.7	59.2
Sat	11/11/17	59.5	63.0	59.5	59.9	57.7	57.1

Northern Line Extension Main Works Contract

Table 4

Monthly Noise Levels at R2 & R3									
		Lmorn	Lday	Leve	Max LEN	Max LLN	Typical LLN		
Sun	15/10/17	-	67.2	-	68.2	68.2	65.8		
Mon	16/10/17	68.9	69.3	68.2	66.9	70.5	66.1		
Tue	17/10/17	69.2	70.2	73.3	67.8	68.4	65.8		
Wed	18/10/17	69.0	72.1	70.0	67.9	69.5	67.3		
Thu	19/10/17	69.4	70.9	73.2	68.1	70.7	68.2		
Fri	20/10/17	70.1	72.2	68.3	68.4	67.8	67.2		
Sat	21/10/17	68.6	69.7	67.5	73.2	66.7	65.5		
Sun	22/10/17	-	67.5	-	69.0	68.4	65.9		
Mon	23/10/17	68.8	72.9	68.6	67.5	68.1	65.7		
Tue	24/10/17	69.1	73.2	68.3	68.2	75.4	68.5		
Wed	25/10/17	69.0	73.2	71.7	67.7	68.5	66.4		
Thu	26/10/17	69.3	73.8	72.7	68.8	73.5	68.5		
Fri	27/10/17	69.4	71.6	70.1	68.7	68.0	66.9		
Sat	28/10/17	68.2	71.3	67.7	70.5	67.9	66.4		
Sun	29/10/17	-	67.7	-	68.6	69.0	65.9		
Mon	30/10/17	69.8	72.0	71.0	68.4	68.8	66.2		
Tue	31/10/17	70.3	71.6	69.1	67.8	68.7	66.7		
Wed	01/11/17	69.5	71.1	68.8	67.6	69.1	66.7		
Thu	02/11/17	69.6	70.1	68.7	67.6	69.0	66.8		
Fri	03/11/17	69.1	70.3	68.1	67.4	68.9	67.3		
Sat	04/11/17	68.4	70.1	66.4	69.4	67.6	66.4		
Sun	05/11/17	-	68.0	-	69.3	69.2	65.7		
Mon	06/11/17	69.2	69.9	68.8	68.6	68.9	66.0		
Tue	07/11/17	69.3	71.4	68.9	69.9	70.1	68.1		
Wed	08/11/17	69.1	70.5	68.9	67.6	68.7	66.6		
Thu	09/11/17	69.4	70.4	68.4	67.6	68.5	66.6		
Fri	10/11/17	69.2	70.2	69.5	68.2	69.3	68.5		
Sat	11/11/17	70.1	70.7	68.1	68.7	67.9	67.5		

Northern Line Extension Main Works Contract

Table 5

Monthly N	Noise Levels at R	4					
		Lmorn	Lday	Leve	Max LEN	Max LLN	Typical LLN
Sun	15/10/17	-	_*	-	_*	_*	_*
Mon	16/10/17	_*	67.5	65.7	59.2	58.2	53.0
Tue	17/10/17	63.8	67.7	60.4	57.2	58.5	53.6
Wed	18/10/17	62.7	68.4	60.8	58.1	58.0	54.0
Thu	19/10/17	61.8	69.3	65.6	56.8	58.3	53.9
Fri	20/10/17	62.6	70.2	69.0	56.7	55.6	52.4
Sat	21/10/17	63.1	68.0	_*	67.3	_*	_*
Sun	22/10/17	-	-*	-	_*	-*	-*
Mon	23/10/17	_*	_*	_*	_*	_*	_*
Tue	24/10/17	_*	_*	_*	_*	_*	_*
Wed	25/10/17	_*	_*	_*	_*	_*	_*
Thu	26/10/17	_*	_*	_*	_*	_*	_*
Fri	27/10/17	_*	_*	_*	_*	_*	_*
Sat	28/10/17	_*	_*	_*	_*	_*	_*
Sun	29/10/17	-	_*	-	_*	_*	_*
Mon	30/10/17	_*	69.1	68.1	53.8	55.5	52.1
Tue	31/10/17	63.1	68.7	66.6	55.2	55.4	51.9
Wed	01/11/17	64.8	69.6	67.5	54.7	64.0	53.6
Thu	02/11/17	64.1	65.2	65.5	60.9	55.4	52.4
Fri	03/11/17	63.1	67.9	66.2	52.9	53.5	50.8
Sat	04/11/17	61.6	69.1	53.0	60.8	54.8	50.0
Sun	05/11/17	-	55.7	-	57.7	56.2	49.4
Mon	06/11/17	57.9	67.9	66.6	58.7	56.0	50.1
Tue	07/11/17	63.2	67.1	64.3	53.9	56.6	51.3
Wed	08/11/17	59.2	65.3	63.5	54.7	55.5	51.2
Thu	09/11/17	56.5	64.3	65.7	55.9	55.6	51.5
Fri	10/11/17	56.1	65.2	63.4	55.0	55.3	51.7
Sat	11/11/17	58.8	66.4	55.3	65.3	50.5	49.9

^{*}No data due to a monitor malfunctioning.

Northern Line Extension Main Works Contract

4 TRIGGER RESPONSE LOG

Exceedances above the limits set out in the Noise and Vibration Mitigation Scheme, included as **Appendix II** are identified along with the action taken in **Table 6** below:

Table 6

	NOISE TRIGGER LOG									
•	Date	Recept or	Time period	Noise Level L _{Aeq,T} , dB (exceedance above trigger level	Cause	Best Practicable Means check				
	21/10/17	R2/R3	LEN	73.2 (+0.3)	Three motorbikes engines.	n/a				
	24/10/17	R2/R3	LLN	75.4 (+0.9)	Motorbikes engines, emergency sirens and general traffic noise.	n/a				

No exceedances occurred during the monitoring period due to the NLE activities.

Northern Line Extension Main Works Contract

APPENDIX I - SITE PLAN

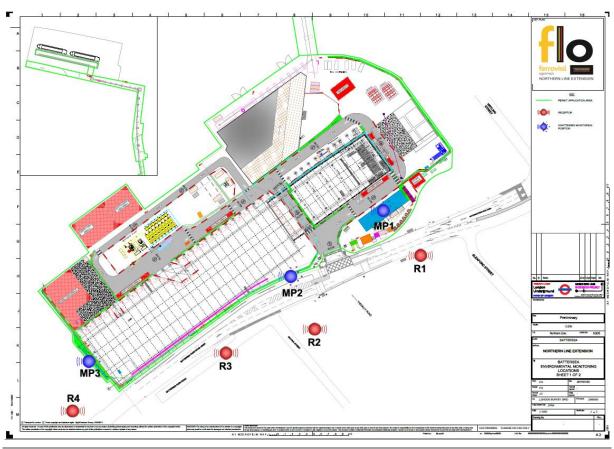


Figure 1 – NLE site plan and sensitive receptor locations

Northern Line Extension Main Works Contract

APPENDIX II – NORTHERN LINE EXTENSION: CONSTRUCTION NOISE AND VIBRATION MITIGATION SCHEME

Noise Insulation

A dwelling will be eligible for noise insulation where the total noise level due to construction of the railway (pre-existing ambient plus airborne NLE construction noise), measured or predicted at a point one metre in front of the most exposed of any windows and doors in any façade of a building which is an eligible dwelling, exceeds whichever is the higher of either: a) any of the following criteria in **Table 7**.

Table 7

NOISE INSULATION TRIGGER LEVEL TABLE								
Time	Relevant Time Period	Averaging Time Period	Noise Insulation Trigger Level (L _{Aeq} , _T) dB					
	07:00 - 08:00	1 hr	70					
	08:00 - 18:00	10 hr	75					
Monday to Friday	18:00 - 19:00	1 hr	70					
	19:00 - 22:00	3 hr	65					
	22:00 - 07:00	1 hr	55					
	07:00 - 08:00	1 hr	70					
	08:00 - 13:00	5 hr	75					
Saturday	13:00 – 14:00	1 hr	70					
	14:00 - 22:00	3 hr	65					
	22:00 - 07:00	1 hr	55					
Sunday and Public	07:00 - 22:00	1 hr	65					
Holidays	22:00 - 07:00	1 hr	55					

Or

(b) 5 dB above the pre-existing airborne noise level for the corresponding times of day (i.e. the Relevant Time Periods presented in column 2 of Table 7);

And

for a period of 10 or more days of working in any 15 consecutive days or for a period of 3 or more nights (22:00-07:00) of working in any 7 consecutive nights or for a total of days exceeding 40 in any six consecutive months.

Northern Line Extension Main Works Contract

APPENDIX III - BASELINE SURVEY

Attended Survey

Baseline noise measurements were taken in the area surrounding the Battersea worksite in October 2014. Measurement locations and results can be seen below; locations were chosen in order to cover the closest sensitive receptors around the ventilation shaft site. Further details related to the exercise are documented in the report 'T2385.1 – Northern Line Extension: Pre-construction Noise and Vibration Baseline Report'.

Table 8

ATTENDED E	ATTENDED BASELINE RESULTS								
ID	Address	Time Period	Typical L _{Aeq,T} dB						
		Daytime	76.0						
BS1	169 Battersea Park Road, Battersea	Evening	68.3						
	Ballersea	Night-time	64.2						
	Viridian Apartments,	Daytime	78.5						
BS2	Battersea Park Road,	Evening	73.1						
	Battersea	Night-time	63.0						
		Daytime	67.6						
BS3	188 Kirtling Street, Battersea	Evening	66.9						
	Ballorood	Night-time	59.3						
		Daytime	60.2						
BS4	Howard Bldg., Chelsea Bridge Wharf, Battersea	Evening	60.9						
	Briago Whall, Ballorood	Night-time	51.2						

Unattended Survey

In order to assess typical ambient noise levels outside core hours, data has been gathered by the monitoring system in place at the Battersea worksite. These levels have been taken from the period between 11th January 2016 and 3rd April 2016.

Table 9

UNATTENDED BASELINE RESULTS									
	M-F 1900- 2200	M-F 2200- 0700	Sat 1400- 2200	Sat 2200- 0700	Sun 0700- 2200	Sun 2200- 0700			
	(LEN)	(LLN)	(LEN)	(LLN)	(LEN)	(LLN)			
	L _{Aeq,T} dB	$L_{\text{Aeq},T} dB$	$L_{Aeq,T} dB$	$L_{Aeq,T} dB$	$L_{Aeq,T} dB$	L _{Aeq,T} dB			
R1	70.9	69.5	70.7	67.9	70.1	68.0			
R2/R3	70.9	69.5	70.7	67.9	70.1	68.0			
R4	68.3	64.2	68.3	64.2	68.3	64.2			

Northern Line Extension Main Works Contract

Trigger Levels

Trigger levels for each receptor, as stated in the Northern Line Extension: Construction Noise and Vibration Mitigation Scheme (**Appendix II**) can be seen in **Table 10** below:

Table 10

TRIGGER LEVELS									
	Core Hours, L _{Aeq,T} dB	M-F 07:00-08:00 18:00-19:00 (Lmorn, Leve) LAeq,T dB	M-F 19:00- 22:00 (LEN) L _{Aeq,T} dB	M-F 22:00- 07:00 (LLN) L _{Aeq,T} dB	Sat 14:00- 22:00 (LEN) L _{Aeq,T} dB	Sat 22:00- 07:00 (LLN) L _{Aeq,T} dB	Sun 07:00- 22:00 (LEN) L _{Aeq,T} dB	Sun 22:00- 07:00 (LLN) L _{Aeq,T} dB	
R1	83.5	78.1	75.9	74.5	75.7	72.9	75.1	73.0	
R2/R3	83.5	78.1	75.9	74.5	75.7	72.9	75.1	73.0	
R4	81.0	73.3	73.3	69.2	73.3	69.2	73.3	69.2	

Northern Line Extension Main Works Contract

APPENDIX IV - GLOSSARY

Table 11

ABBREVIATIONS	
L _{morn}	Morning values from 07:00 to 08:00 Monday to Saturday.
L _{day}	Core hours from 08:00 to 18:00 Monday to Friday, 08:00 to 13:00 Saturday. 07:00 to 21:00 on Sunday is included but not considered to be Core hours.
Leve	Evening values from 18:00 to 19:00 Monday to Friday and from 13:00 to 14:00 Saturday.
Max LEN	Maximum early night values from 19:00 to 22:00 Monday to Friday, 14:00 to 22:00 Saturday and from 07:00 to 22:00 Sun.
Max LLN	Maximum late night values from 22:00 to 07:00 Monday to Sunday.
Typical LLN	Arithmetic average of the intervals for the late night time period.
